

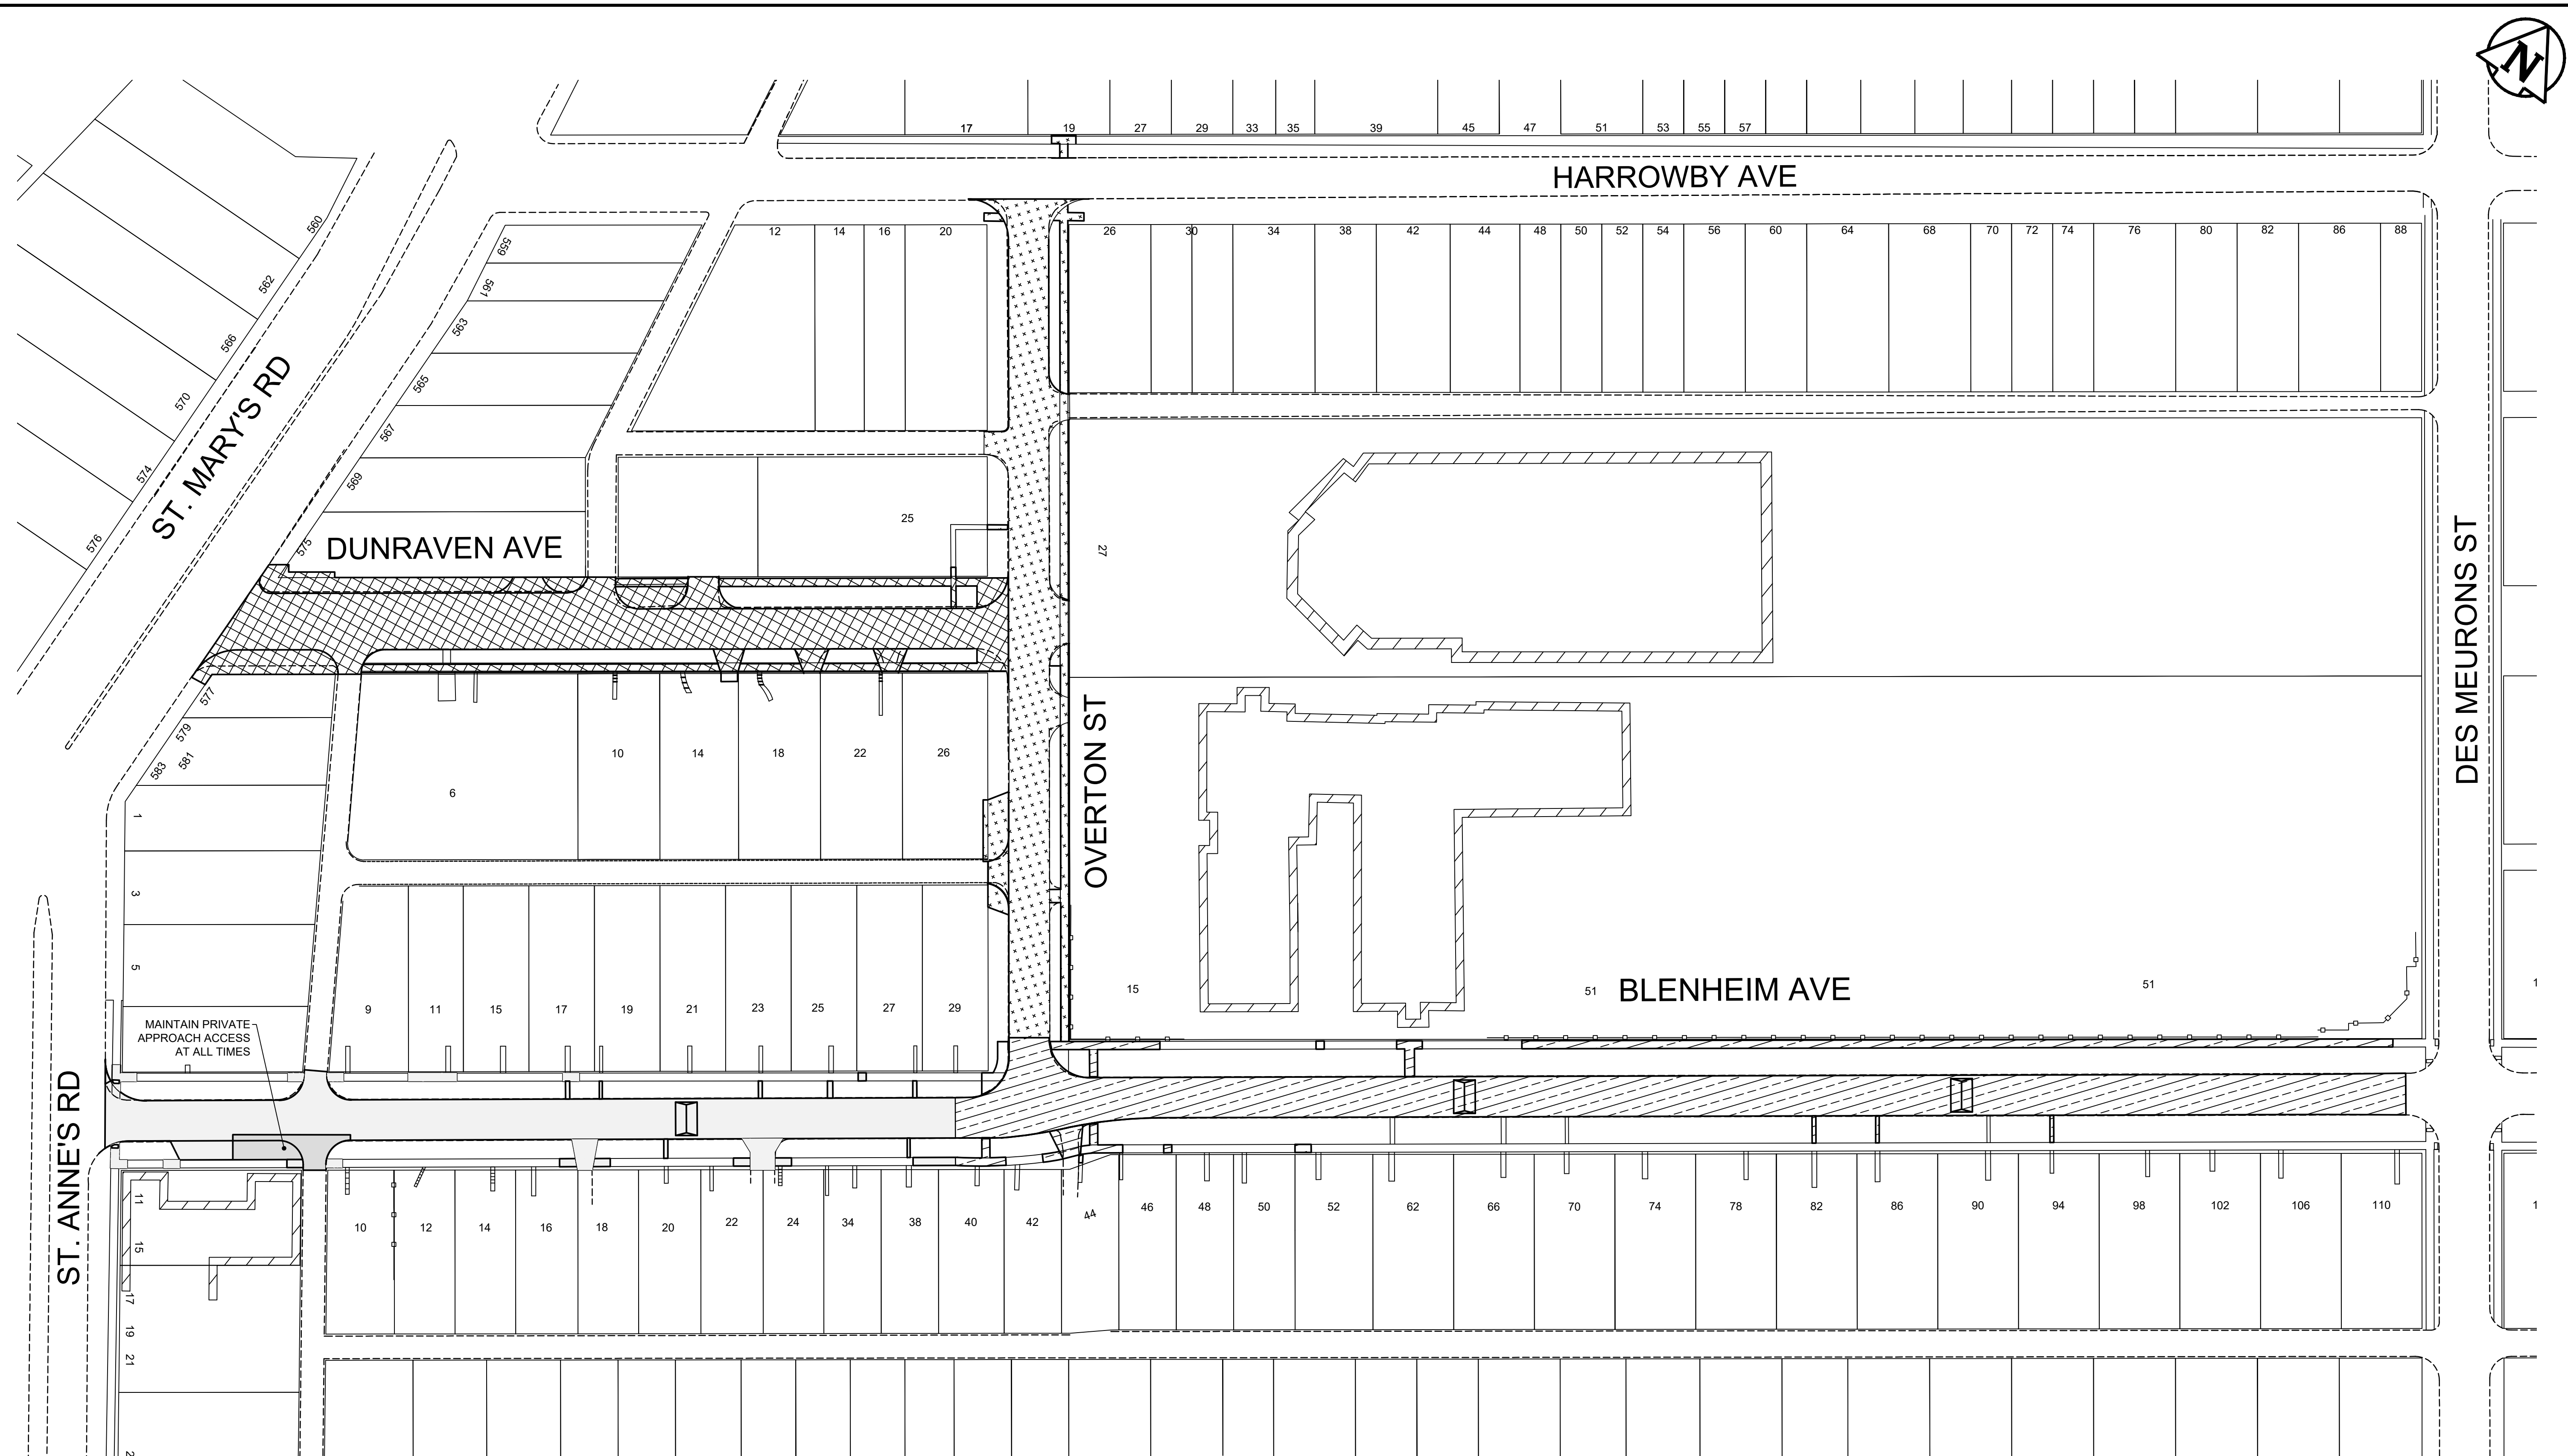


APPENDIX 'J' – CONSTRUCTION STAGING DRAWING



STAGING LEGEND



- BLENHEIM AVE STAGE 1: WORK TO BE COMPLETED NO LATER THAN 07/01/2024
- BLENHEIM AVE STAGE 2: WORK TO BE COMPLETED NO LATER THAN 09/01/2024
- OVERTON ST: WORK TO BE COMMENCED NO EARLIER THAN 07/01/2024 AND COMPLETED NO LATER THAN 09/01/2024
- DUNRAVEN AVE: WORK TO BE COMMENCED UPON COMPLETION OF WORK ON OVERTON ST

FOR INFORMATION ONLY

TENDER NO. 4-2024



THE CITY OF WINNIPEG
PUBLIC WORKS DEPARTMENT

CONSTRUCTION STAGING

SEQUENCE OF WORK FOR BLENHEIM AVE,
OVERTON ST AND DUNRAVEN AVE,
ASPHALT RECONSTRUCTION

SHEET 1 OF 1
