


WATER SERVICE INFORMATION


ADDRESS	SIZE (mm) MATERIAL (STREET)	SIZE (mm) MATERIAL (PROP.)	SHORT & LONG MEASUREMENT	CORP. LOCATION	REMARKS
100 SUMMERFIELD WAY	-	-	4.35 WEL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	71.079 WML OF SUMMERFIELD WAY (E-LEG)	-	-
101 SUMMERFIELD WAY	-	-	6.08 EWL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	61.042 WML OF SUMMERFIELD WAY (E-LEG)	-	-
104 SUMMERFIELD WAY	-	-	4.90 WEL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	56.176 WML OF SUMMERFIELD WAY (E-LEG)	-	-
105 SUMMERFIELD WAY	-	-	4.96 EWL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	44.985 WML OF SUMMERFIELD WAY (E-LEG)	-	-
108 SUMMERFIELD WAY	-	-	3.33 WEL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	39.747 WML OF SUMMERFIELD WAY (E-LEG)	-	-
109 SUMMERFIELD WAY	-	-	6.29 WEL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	29.370 WML OF SUMMERFIELD WAY (E-LEG)	-	-
112 SUMMERFIELD WAY	-	-	4.39 WEL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	25.471 WML OF SUMMERFIELD WAY (E-LEG)	-	-
113 SUMMERFIELD WAY	20	-	4.24 EWL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	CU	CU	13.916 WML OF SUMMERFIELD WAY (E-LEG)	5.1 W OF S/C	-
116 SUMMERFIELD WAY	20	-	4.61 WEL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	CU	CU	8.530 WML OF SUMMERFIELD WAY (E-LEG)	0.6 E OF S/C	-
117 SUMMERFIELD WAY	20	-	3.44 EWL HSE	17.2	RECONNECT SERVICE
RESIDENTIAL	CU	CU	3.035 NNL OF SUMMERFIELD WAY (N-LEG)	3.8 W OF S/C	-
121 SUMMERFIELD WAY	20	-	2.99 SNL HSE	13.6	RECONNECT SERVICE
RESIDENTIAL	CU	CU	11.455 EWL OF SUMMERFIELD WAY (E-LEG)	13.9 W OF S/C	-
125 SUMMERFIELD WAY	-	-	6.06 SNL HSE	N/A	RECONNECT SERVICE
RESIDENTIAL	-	CU	19.558 EWL OF SUMMERFIELD WAY (E-LEG)	-	-

(1) LINEAR DISTANCE FROM THE S/C TO THE CORP USED ALONG BENDS & CURVED R.O.W.
 (2) DIRECTION FROM S/C
 * SERVICES TO BE RENEWED TO R, ALL OTHERS TO BE RECONNECTED

NOTE: CHAINAGES SHOWN ARE ALONG N. R. OF SUMMERFIELD WAY (N-LEG)

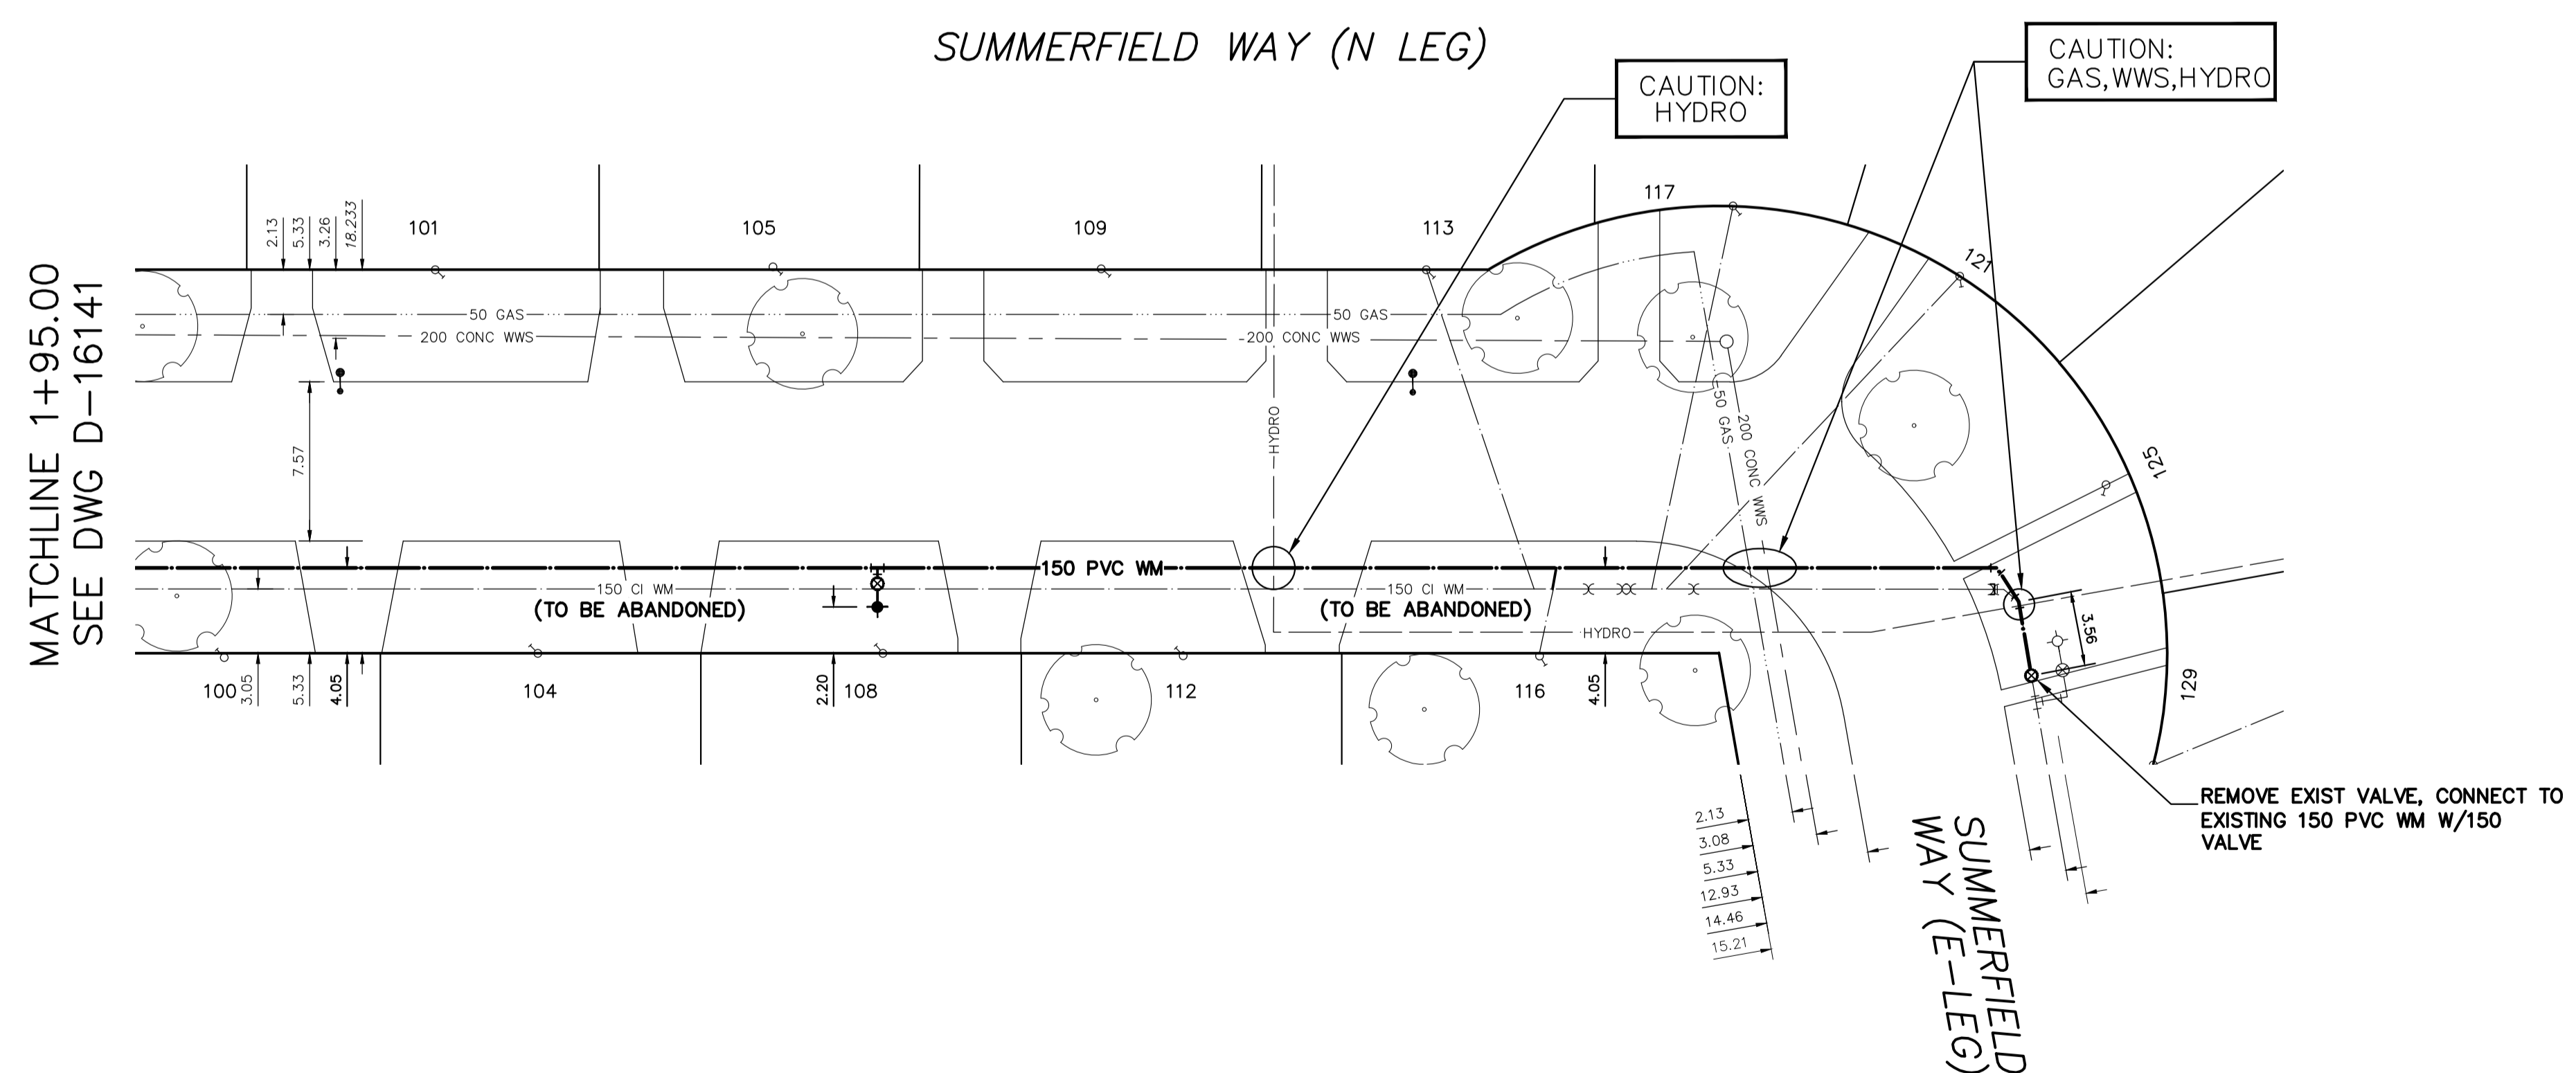

MATCHLINE 1+95.00
SEE DWG D-16141

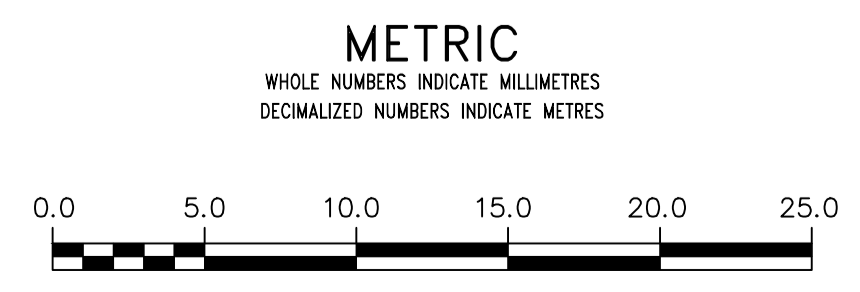

WARNING
 IF POWER EQUIPMENT OR EXPLOSIVES ARE TO BE USED FOR EXCAVATION ON THIS PROJECT THE CONTRACTOR MUST:
 1) NOTIFY THE GAS COMPANY OF THE PROPOSED LOCATION OF EXCAVATION.
 2) TAKE PRECAUTION TO AVOID DAMAGE TO GAS COMPANY INSTALLATIONS.
 SEE PROVINCIAL REGULATION 210/72 FOR DETAILS

LOCATION APPROVED
 UNDERGROUND STRUCTURES
 SUPV. U/G STRUCTURES COMMITTEE DATE
 NOTE:
 LOCATION OF UNDERGROUND STRUCTURES AS SHOWN ARE BASED ON THE BEST INFORMATION AVAILABLE BUT NO GUARANTEE IS GIVEN THAT ALL EXISTING UTILITIES ARE SHOWN OR THAT THE GIVEN LOCATIONS ARE EXACT. CONFIRMATION OF EXISTENCE AND EXACT LOCATION OF ALL SERVICES MUST BE OBTAINED FROM THE INDIVIDUAL UTILITIES BEFORE PROCEEDING WITH CONSTRUCTION.

VERTICAL DATUM: CGVD28 (HT2.0 Geoid)			
HORIZONTAL DATUM: NAD83 (June 1990), Zone 14			
NO.	REVISIONS	DATE	BY

DESIGNED BY	RG	CHECKED BY	SC
DRAWN BY	AOM	APPROVED BY	KZ
SCALE:		RELEASED FOR CONSTRUCTION	
HORIZONTAL	1:250		
VERTICAL	1:50		
DATE	2022 07 14	DATE	
PLOT DATE:	2022 07 14		

ENGINEER'S SEAL
 CONSULTANT DRAWING NUMBER

THE CITY OF WINNIPEG
 WATER AND WASTE DEPARTMENT
 ENGINEERING DIVISION

2022 WATER MAIN RENEWALS
 CONTRACT 12

SUMMERFIELD WAY (N-LEG)
 97 E OF SUMMERFIELD WAY (W-LEG) TO
 SUMMERFIELD WAY (E-LEG)

SHEET 13 OF 14
 CITY DRAWING NUMBER
 D-16141

FOR INDEX SEE D-16133

NOTE: ALL VALVES TO BE INSTALLED COUNTERCLOCKWISE TO CLOSE
