Winnipeg Water Treatment Plant Project -- Bid Opportunity 171-2006

Revision 1
Date: Jan 3rd 2007
Addendum 4

Schedule SCH #2 for Precast Roof Panel Erection, Topping & Roofing installation.
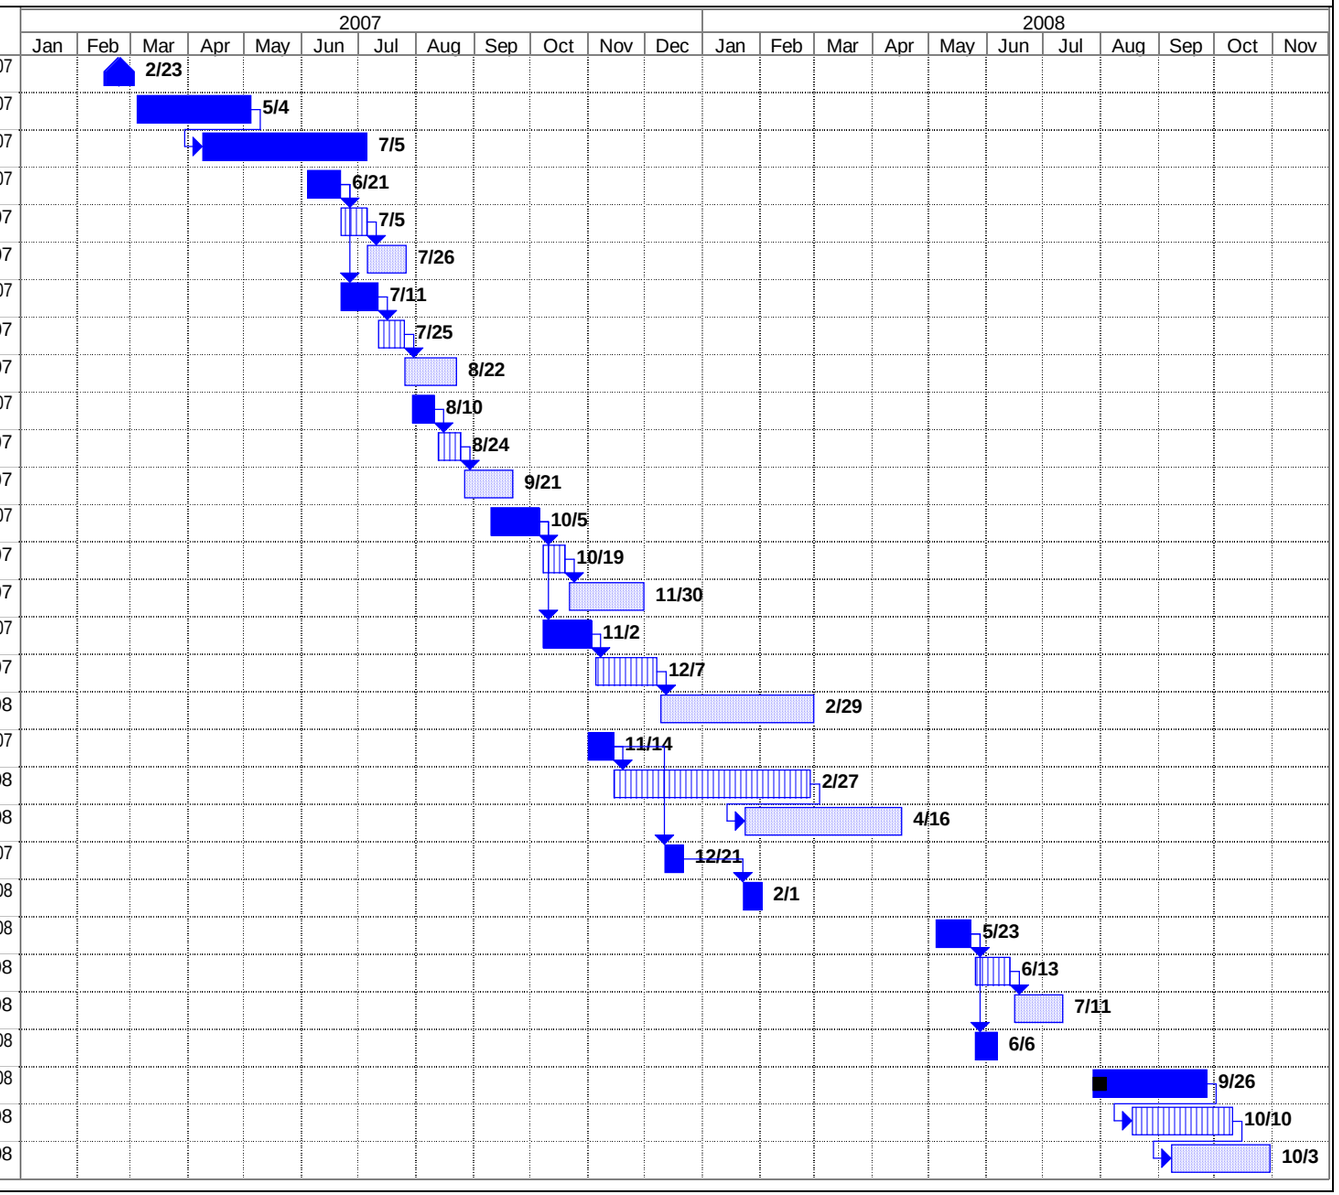
ID	Task Name	Duration	Start	Finish
1	Award Precast Roof Panels Contract	1 day	Fri 2/23/07	Fri 2/23/07
2	Shop Drawing Review period	45 days	Mon 3/5/07	Fri 5/4/07
4	Manufacture Precast panels	64 days	Mon 4/9/07	Thu 7/5/07
5	Erect panels to WI area	14 days	Mon 6/4/07	Thu 6/21/07
6	Install conc. toppings to Area WI	10 days	Fri 6/22/07	Thu 7/5/07
7	Install VB, insulation and roofing work (WI)	15 days	Fri 7/6/07	Thu 7/26/07
8	Erect panels to WM area	14 days	Fri 6/22/07	Wed 7/11/07
9	Install conc.toppings to Area WM	10 days	Thu 7/12/07	Wed 7/25/07
10	Install VB, insulation and roofing work (WM)	20 days	Thu 7/26/07	Wed 8/22/07
11	Erect Panels to WA Area	10 days	Mon 7/30/07	Fri 8/10/07
12	Install conc. toppings to Area WA	10 days	Mon 8/13/07	Fri 8/24/07
13	Install VB, insulation and roofing work (WA)	20 days	Mon 8/27/07	Fri 9/21/07
14	Erect Panels to WO Area	20 days	Mon 9/10/07	Fri 10/5/07
15	Install conc. toppings to Area WO	10 days	Mon 10/8/07	Fri 10/19/07
16	Install VB, insulation and roofing work (WO)	30 days	Mon 10/22/07	Fri 11/30/07
17	Erect Panels to WR Area	20 days	Mon 10/8/07	Fri 11/2/07
18	Install conc. toppings to WR Area	25 days	Mon 11/5/07	Fri 12/7/07
19	Install VB, insulation and roofing work (WR)	60 days	Mon 12/10/07	Fri 2/29/08
20	Erect panels to WF area (Grids B1 to B8)	10 days	Thu 11/1/07	Wed 11/14/07
21	Install conc. toppings to WF Area	75 days	Thu 11/15/07	Wed 2/27/08
22	Install VB, insulation and roofing work (WF)	60 days	Thu 1/24/08	Wed 4/16/08
23	Erect panels to WF area (Grids B8 to B15)	8 days	Wed 12/12/07	Fri 12/21/07
25	Erect panels to WF area (Grids B15 to B18)	8 days	Wed 1/23/08	Fri 2/1/08
26	Erect Panels to WC area	15 days	Mon 5/5/08	Fri 5/23/08
27	Install conc. Toppings to WC Area (WC)	15 days	Mon 5/26/08	Fri 6/13/08
28	Install VB, insulation and roofing work (WC)	20 days	Mon 6/16/08	Fri 7/11/08
29	Erect Hollow Core slabs to WP area	10 days	Mon 5/26/08	Fri 6/6/08
30	Erect panels to WP area (Grids B2 to B19)	45 days	Mon 7/28/08	Fri 9/26/08
31	Install conc toppings to WP Area	40 days	Mon 8/18/08	Fri 10/10/08
32	Install VB, insulation and roofing work (WP)	39 days	Mon 9/8/08	Thu 10/30/08
