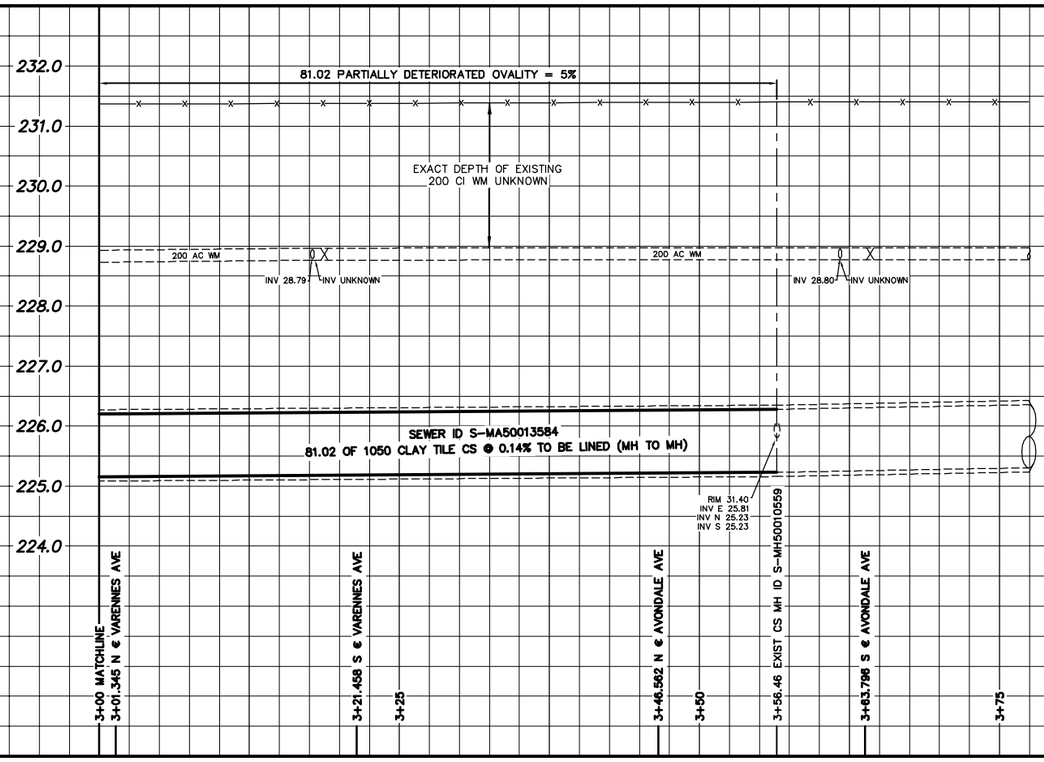

SEWER SERVICE INFORMATION

ADDRESS	SIZE	P DIST JUNCTION TIE
145 ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
147 ST ANNES RD RESIDENTIAL		– 21.98 S OF MH @ BANK AVE
149 ST ANNES RD RESIDENTIAL		– 33.44 S OF MH @ BANK AVE
153 ST ANNES RD RESIDENTIAL		– 43.95 S OF MH @ BANK AVE
155 ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
156 ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
156B ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
157 ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
158 ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
159 ST ANNES RD RESIDENTIAL		– 64.98 S OF MH @ BANK AVE
160 ST ANNES RD COMMERCIAL		– NO INFORMATION AVAILABLE
160A ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE
167 ST ANNES RD RESIDENTIAL		– 12.10 S OF MH @ AVONDALE AVE
170 ST ANNES RD RESIDENTIAL		– NO INFORMATION AVAILABLE

NOTE: CHAINAGES SHOWN ARE ALONG E € OF ST ANNES ROAD.

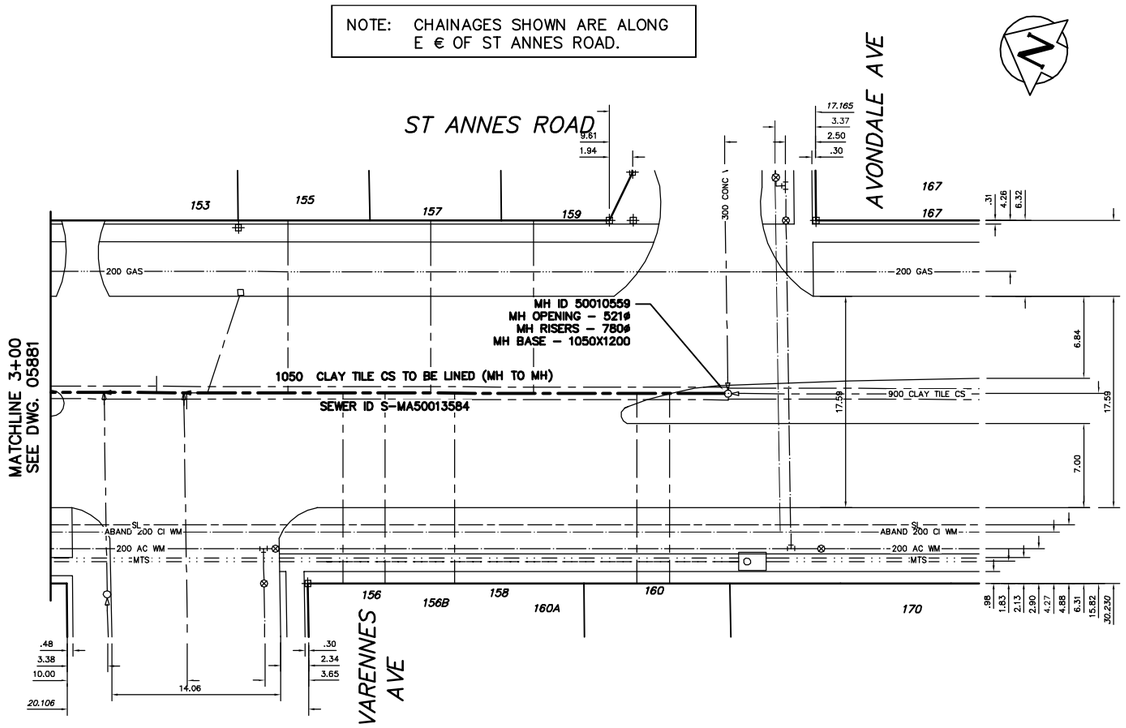

SEWER JUNCTION INFORMATION FROM SEWER VIDEO INSPECTION SEWER ID S-MA50013584

DISTANCE FROM MH ID S-MH50010559

4.90	N	150	WEST	JN
7.60	N	150	WEST	JN
16.20	N	150	EAST	JN
22.80	N	150	WEST	JN
24.80	N	150	EAST	JN
28.60	N	150	WEST	JN
32.10	N	150	WEST	JN
36.70	N	150	EAST	JN
43.40	N	150	EAST	JN
45.10	N	150	WEST	JN
47.60	N	150	EAST	JN
52.00	N	450 CONC WWS	WEST	JN

METRIC
WHOLE NUMBERS INDICATE MILLIMETRES
DECIMALIZED NUMBERS INDICATE METRES

WARNING

IF POWER EQUIPMENT OR EXPLOSIVES ARE TO BE USED FOR EXCAVEEATION ON THIS PROJECT THE CONTRACTOR MUST:
1) NOTIFY THE GAS COMPANY OF THE PROPOSED LOCATION OF EXCAVEEATION.
2) TAKE PRECAUTION TO AVEEOID DAMAGE TO GAS COMPANY INSTALLATIONS.

SEE PROVINCIAL REGULATION 210/72 FOR DETAILS

0.0 5.0 10.0 15.0 20.0 25.0

200 WM	WATERMAIN	200 WM		SL , HYDRO		150 WM	WATERMAIN	150 WM
✧	HYDRANT	✦		MTS		t	HYDRANT	t
⊗	VALVE	⊗		TRAFFIC SIGNALS		X	VALVE	X
525 LDS	LAND DRAINAGE SEWER	525 LDS	50 GAS	GAS	50 GAS	300 LDS	LAND DRAINAGE SEWER	300 LDS
375 WWS	WASTEWATER SEWER	375 WWS		SURVEY BAR		250 WWS	WASTEWATER SEWER	250 WWS
○	MANHOLE	●		FENCE			PROFILE	
□	CATCH BASIN	■		POLE – HYDRO, MTS			GROUND ABOVE PIPE	
▽	CURB INLET	▼		CURB STOP			? DITCH (NORTH & WEST)	
	JUNCTIONS			GUY ANCHOR			? DITCH (SOUTH & EAST)	
	CULVERT			LIGHT STANDARD			GUTTER (NORTH & WEST)	
	ANODE			TREE			GUTTER (SOUTH & EAST)	
EXISTING	LEGEND–PLAN	PROPOSED	EXISTING	LEGEND–PLAN	PROPOSED	EXISTING	LEGEND–PROFILE	PROPOSED

LOCATION APPROVED
UNDERGROUND STRUCTURES

SUPV. U/G STRUCTURES COMMITTEE — DATE

NOTE:
LOCATION OF UNDERGROUND STRUCTURES AS SHOWN ARE BASED ON THE BEST INFORMATION AVAILABLE BUT NO GUARANTEE IS GIVEN THAT ALL EXISTING UTILITIES ARE SHOWN OR THAT THE GIVEN LOCATIONS ARE EXACT. CONFIRMATION OF EXISTENCE AND EXACT LOCATION OF ALL SERVICES MUST BE OBTAINED FROM THE INDIVIDUAL UTILITIES BEFORE PROCEEDING WITH CONSTRUCTION.

B.M. ELEV. | FIELD BOOK #:
POSTED TO LBIS

NO.	REVISIONS	DATE	BY

CITY OF WINNIPEG
WATER AND WASTE
ENGINEERING DIVISION

DESIGNED BY	TW/SC	CHECKED BY	TW/KZ
DRAWN BY	RMC/TLS	APPROVED BY	KZ
HOR. SCALE	1:250	RELEASED FOR CONSTRUCTION	
VERTICAL	1:50		
DATE	2006 06 28	DATE	

ENGINEER'S SEAL

ORIGINAL SIGNED BY
S.R.J. COURNOYER
06/06/29

BID OPPORTUNITY: 429–2006
FILENAME: 05880_81_82.dwg
PLOT DATE: 2006 06 28

Winnipeg

THE CITY OF WINNIPEG
WATER AND WASTE DEPARTMENT

2006 COMBINED SEWER RENEWALS
BY CIPP LINING

ST ANNE'S ROAD

MH AT BANK AVE TO
MH AT AVONDALE AVE

SHEET 16 OF 29

CITY DRAWING NUMBER
05882
