




PHASE I - STAGE 1 NOTES (GRANT):

- SUGGESTED SCHEDULE
- 5 MONTHS
 - MAY-SEPTEMBER (2017)

- MAJOR CONSTRUCTION ACTIVITIES
1. UTILITY RELOCATIONS (BY OTHERS)
 2. WAVERLEY STREET REHABILITATION BETWEEN MATHERS AND GRANT
 3. GRANT AVENUE WIDENING AND REHABILITATION

- TRAFFIC AND PEDESTRIAN CONTROL
- LANE AT A TIME CONSTRUCTION
 - MAINTAIN PEDESTRIAN TRAFFIC ON AT LEAST ONE SIDE OF GRANT AND ONE SIDE OF WAVERLEY BETWEEN MATHERS AND GRANT AT ALL TIMES

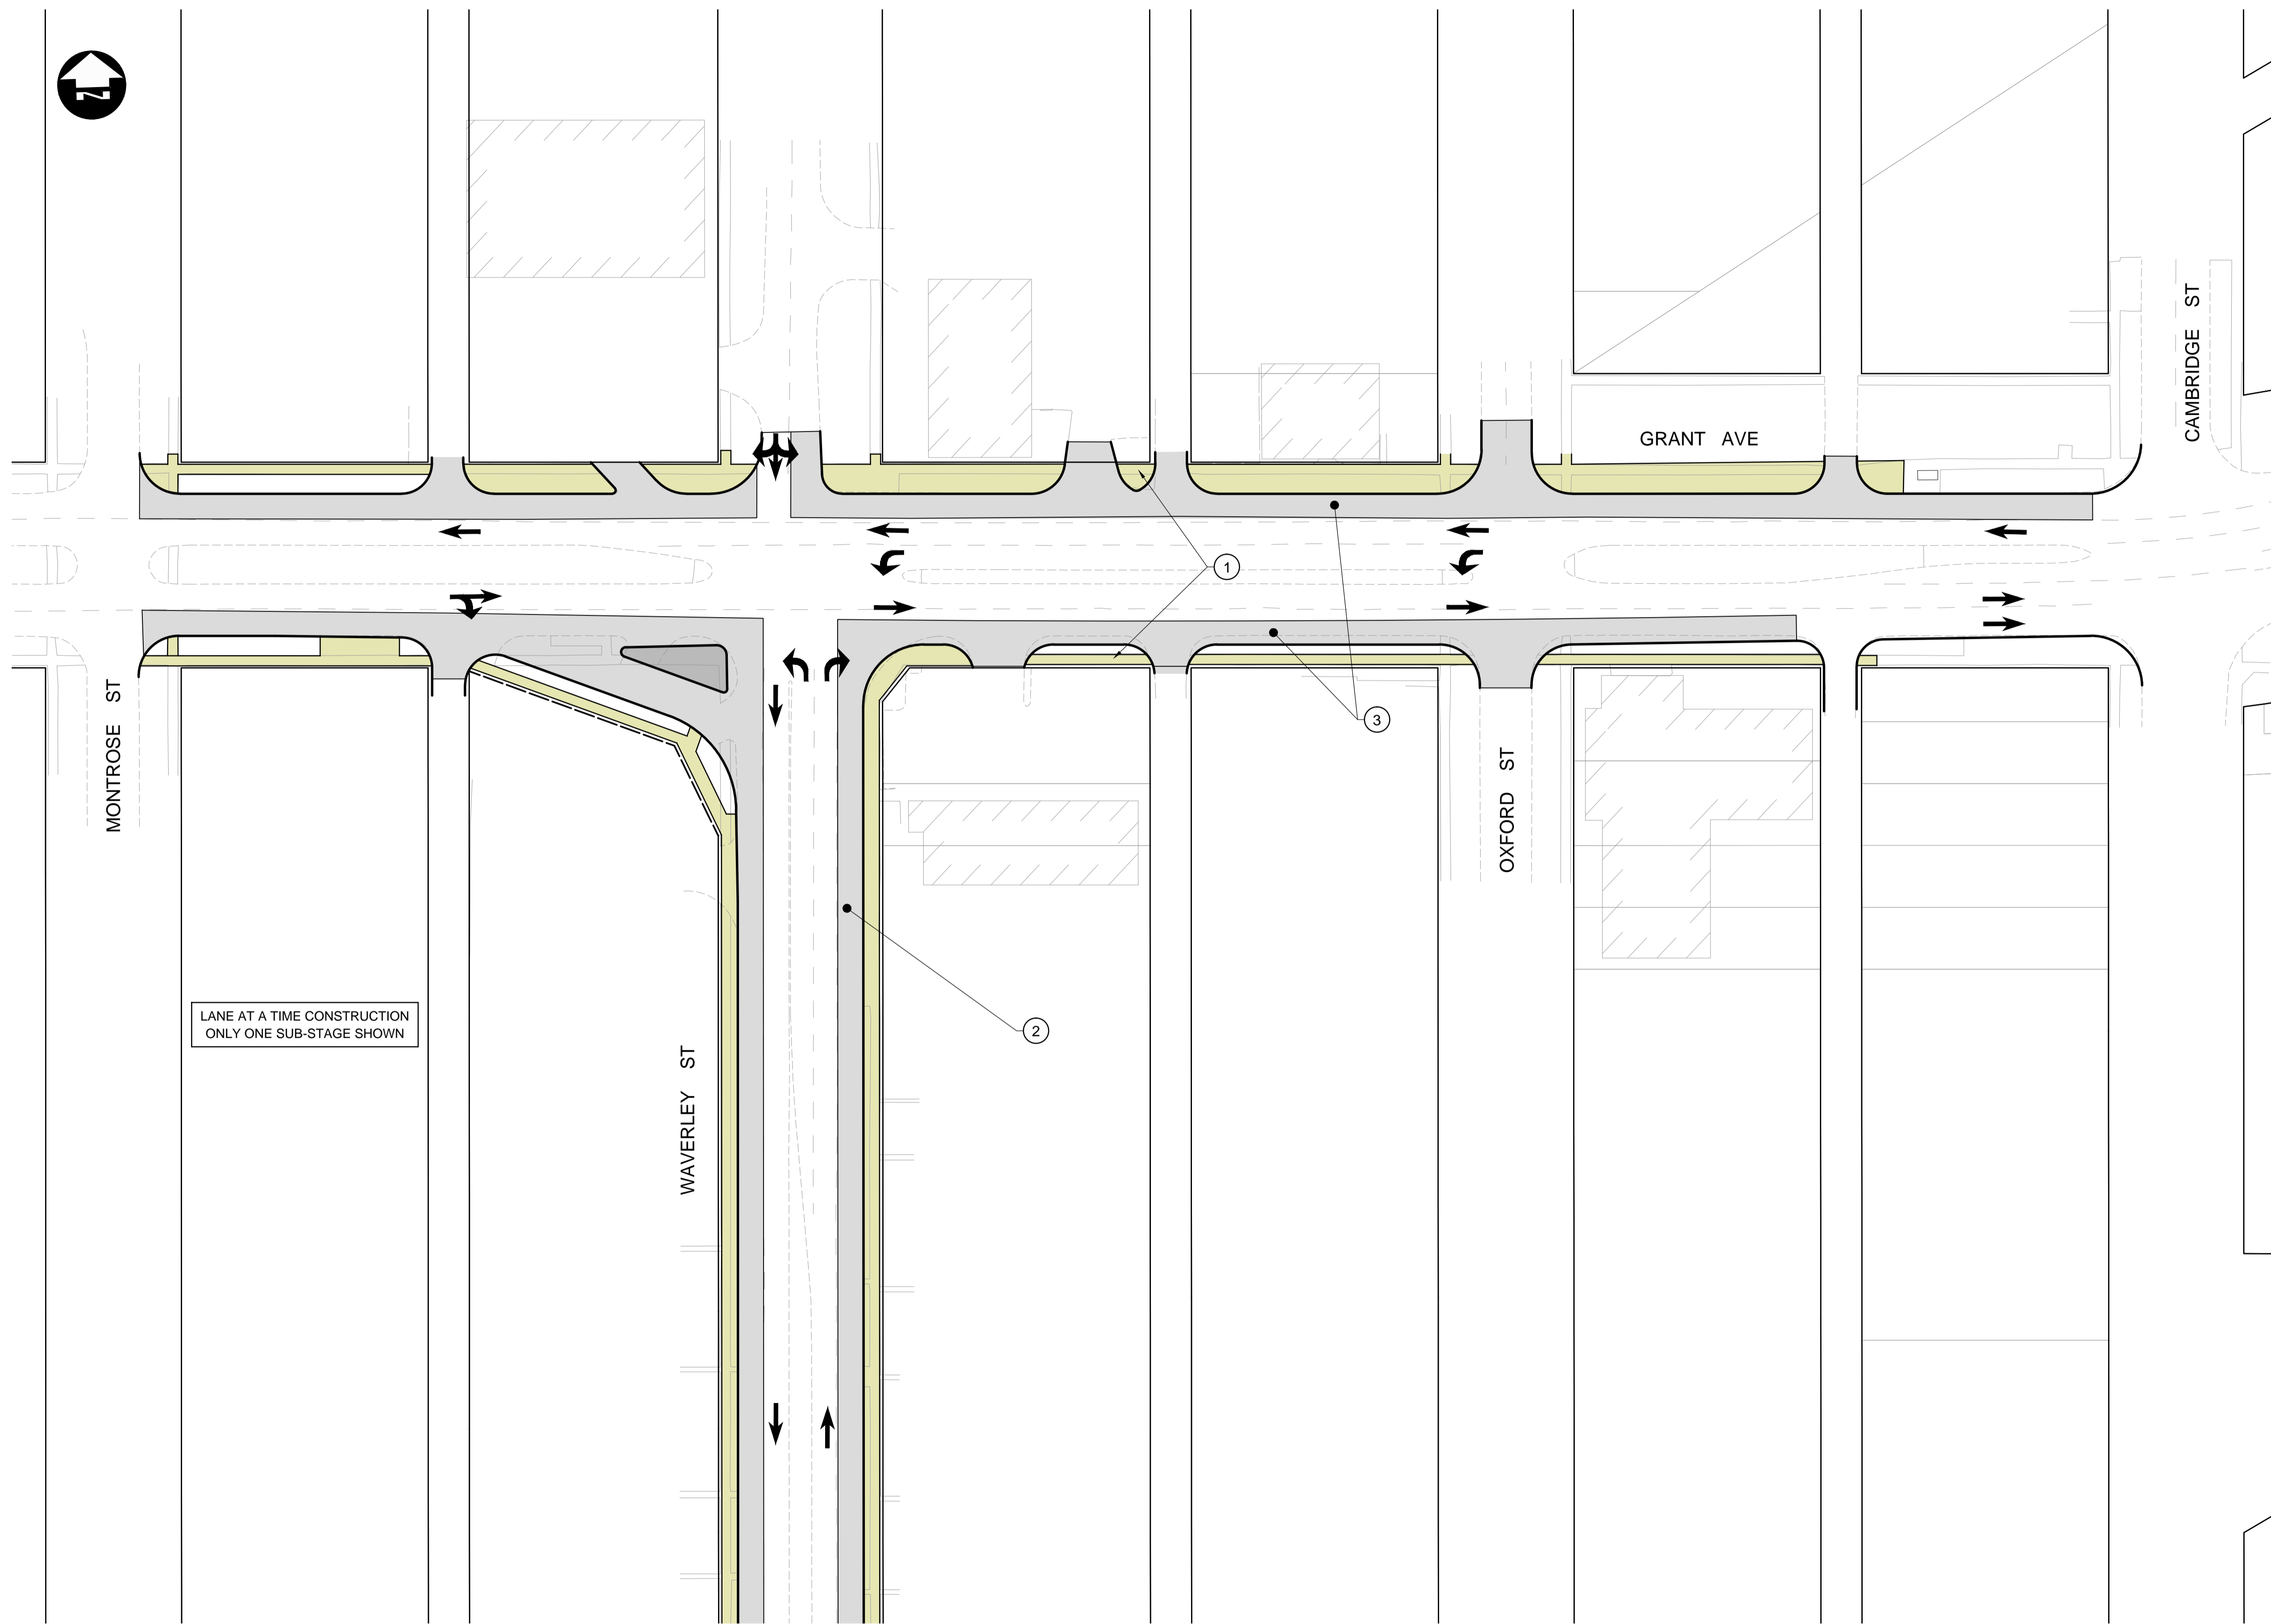

LEGEND - CONSTRUCTION STAGING

	ACTIVE RAILWAY		TEMPORARY ROADWAY CONSTRUCTION		VEHICULAR TRAFFIC
	INACTIVE RAILWAY		TEMPORARY MEDIAN CONSTRUCTION		PEDESTRIAN/CYCLIST TRAFFIC
	SHOOFLY CONSTRUCTION		PERMANENT ROADWAY CONSTRUCTION		LANE CLOSED
	PERMANENT RAILWAY CONSTRUCTION		PERMANENT MEDIAN CONSTRUCTION		SIDEWALK CLOSED
	MAJOR UNDERGROUNDS CONSTRUCTION		TEMPORARY SIDEWALK/MUP CONSTRUCTION		TEMPORARY CROSSING SIGNALS
	EXISTING PROPERTY LINE		PERMANENT SIDEWALK/MUP CONSTRUCTION		
	PROPOSED PROPERTY LINE		BRIDGE CONSTRUCTION		
	CONSTRUCTION EASEMENT		CONTRACTOR LAYDOWN AREA - ACCESS		
			CONTRACTOR LAYDOWN AREA - NO ACCESS		

UNDERGROUND STRUCTURES

SUPPLY	U/G STRUCTURES	DATE

LOCATION OF UNDERGROUND STRUCTURES AS SHOWN ARE BASED ON THE BEST INFORMATION AVAILABLE. BUT NO GUARANTEE IS GIVEN THAT ALL EXISTING UTILITIES ARE SHOWN OR THAT THE GIVEN LOCATIONS ARE EXACT. CONFIRMATION OF EXISTENCE AND EXACT LOCATION OF ALL SERVICES MUST BE OBTAINED FROM THE INDIVIDUAL UTILITIES BEFORE PROCEEDING WITH CONSTRUCTION.

B.M.	ELEV.

NO.	REVISIONS	DATE	BY
0	ISSUED FOR TENDER	17/01/09	DBW

DESIGNED BY	TJH	CHECKED BY	RTP/DBW
DRAWN BY	TJH	APPROVED BY	DBW
HOR. SCALE	1:500	RELEASED FOR CONSTRUCTION	
VERTICAL		DATE	

ENGINEER'S SEAL

CONSULTANT PROJECT NUMBER
16-3353

THE CITY OF WINNIPEG
PUBLIC WORKS DEPARTMENT

Waverley Street Underpass at CN Mile 3.89 Rivers Sub
Contract 2: Underpass Structure, Railworks,
Roadworks, Land Drainage Sewer, Pumping Station
and Landscaping Works

CITY DRAWING NUMBER
U-239-2016-C2-GE-029

SHEET 029 OF 052

CONSULTANT DRAWING NUMBER
C2-GE-029

CONSTRUCTION STAGING
PHASE I - STAGE 1 (4 OF 4)

G:\CAD\163353\Technical\Workspaces\Engineering\Drawings and Figures\Roadworks\Contract\163353-C2-CON-GE-STAGE-1.dwg
